

EXECUTIVE SUMMARY REPORT

Verona Area High School



December 27th, 2019




Topping Pour

Even with the holidays this week, a lot of progress has happened at the Verona Area High School. This past week, we completed the topping slab pour for the whole Atrium! In addition, progress is ongoing for flooring in the library, the large instructional classroom and the fieldhouse. In the performing arts center, we have completed the wood paneling on the front of the stage. Painting also continues as the social stair received its first coat of paint, and the community pool starts the painting process. On the exterior of the school, the metal panels for the main entrance are almost complete too!

The work inside will not be stopping for the new year for in the weeks to come, more progress and finishing stages will be starting. Final cleaning will be starting in the beginning of January to prep for owner furniture to move in. The wall and floor tile in the Community pool will be starting, and flooring in the locker rooms of the fieldhouse. In addition, the kitchen equipment for the level 2 Café mezzanine starts in the beginning of January, and the maple floor in the fieldhouse!

The Past Weeks:

- Athletic flooring in the Fieldhouse
- Atrium Topping Slab
- Painting in the Social Stair
- Diving Well in the pool last wall pour
- Large instructional flooring complete.

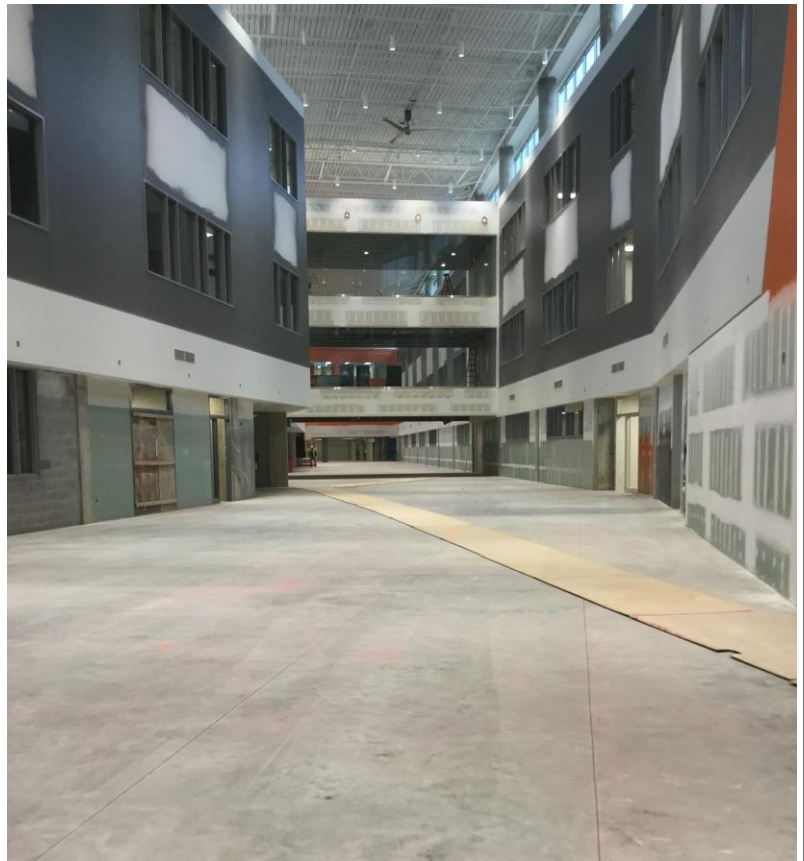

Above: The Atrium topping pour was completed last week Thursday! This pour was over 600 feet long from one end to another, and over 25,000 square feet.

Coming Up in the Weeks Ahead:

- Acoustical panels in the performing arts center
- Final cleaning on Level 3
- Café Mezzanine kitchen equipment
- Final Precast outside of the pool set.
- Completion of Painting in the community pool.



DID YOU KNOW?

Inside the new Verona Area High School, the fieldhouse is covered in three layers of plywood and then the flooring on top. With the fieldhouse being almost 40,000 Square feet, and a plywood sheet being 8'x4', that is 3,750 sheets of plywood inside the fieldhouse!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT

Verona Area High School



December 27th, 2019



Left: The front entrance is completing the finishing touches as the metal panels are finishing up within the next weeks. Lower left is a view inside the large instructional classroom. The patterned carpet was completed this last week.



To the left is a view of the Atrium look outs with the site wood. This last week, the glass handrail was installed. Above is a view into the community pool where painting is underway.

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com



Findorff

EXECUTIVE SUMMARY REPORT

Verona Area High School



December 27th, 2019

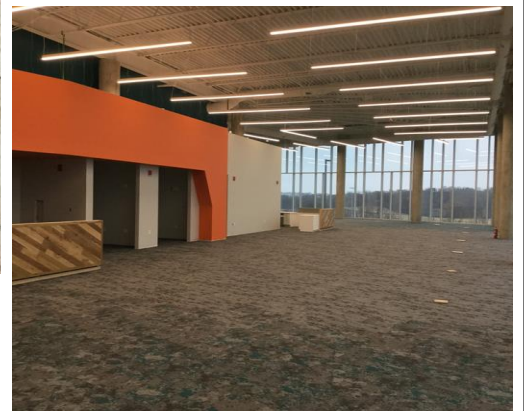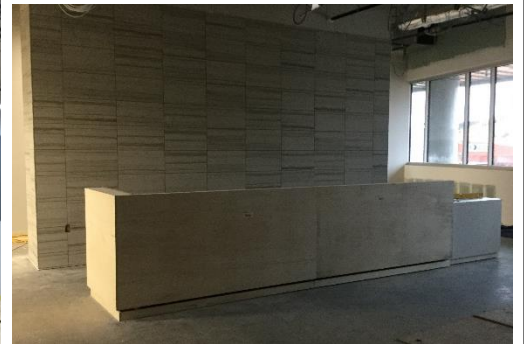

Above is a view from the first floor into the fieldhouse. The first two layers of plywood have been installed, and the final layer of plywood will be installed, and then the maple wood flooring will start. In the upper right corner is a view of the front office. The wall tile has been installed, and the casework is ready for more refurbished wood from the site to be used.



Above is a look into the future library. The lights have been installed, and the carpet is completed. On the left side is a view from the lighting booth. The stage wood paneling is complete along with the Du Chateau wood covering that is completed on the ramps up to the stage.

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff
