

EXECUTIVE SUMMARY REPORT

Verona Area High School



March 8th, 2019



Mark Atrium Decking As Complete!

The Verona Area High School has progressed a lot within the last 2 weeks. One of the major milestones is the completion of the Atrium decking now that the tower crane is removed. In addition, we have poured part of the Kitchen area this last week and continued working on the stud walls and masonry throughout the school.

Major work is planned to start within the next week as the weather starts to turn to Spring. Precast panels will be starting to enclose the Pool areas, and the large joist will start to be set in the Library. In addition, we will be pouring the concrete for the interior social stair next week, and continuing Slab on Grade in both the Art area, and the Core. Finally, the progress will also continue with wall framing, Air Vapor Barrier, Roofing and Masonry.

The Past Weeks:

- Slab on grade Kitchen Area
- Completed Atrium Decking
- CMU walls though out the school
- Stair 3 Steel
- PAC roof decking
- Level 3 East wall framing

Upcoming:

- Library roof Joist
- Level 3 rough in
- Level 3 South Wall framing
- Interior social stair Concrete
- Pool Precast Panels.



The photo above is a view down the atrium from the third floor on the West Bridge. The decking is complete, and the glazing is starting. Below are photos of the Slab on Grade in the Kitchen Area, most of the kitchen is poured, with the rest being poured next week.



DID YOU KNOW?

There are around 670 rooms in this building and around 100 of them are classrooms only!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT


Verona Area High School



March 8th, 2019



Left: The Preforming Arts Center Roof Decking is almost complete! In this photo you can also see the block side of the fire wall between the Pool and the School, along with the joist being set for the Performing Arts Receiving Area. Block Walls also continue throughout the school as shown below are rooms in the fieldhouse locker rooms, and the back up walls around the Maintenance Garage. The bottom right photo also shows the completion of the roof decking in the Fieldhouse!

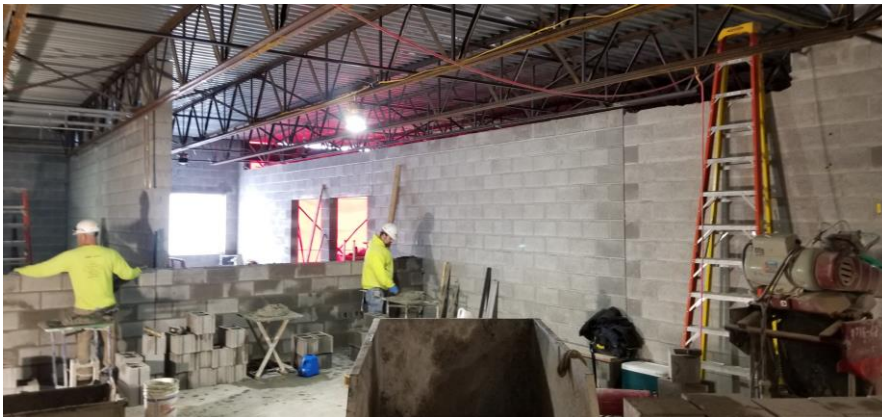

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT


Verona Area High School



March 8th, 2019



Left: The social stair is all ready to be poured on Monday as the rebar and the outlet boxes are installed. Above is a photo of the wall framing and duct work on the third floor. Left is a drone view of the front of the school and the completed sheathing.

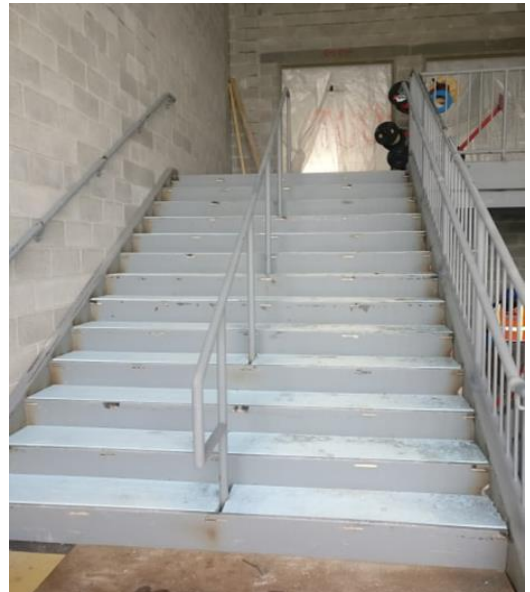

Above: Another set of stairs have been completed! We are using Styrofoam in the pans of the stairs for construction use, and they will be poured with concrete in the future. Left: Views down the main corridor on the third floor, along with a block room that is complete.



QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff
