

EXECUTIVE SUMMARY REPORT

Verona Area High School



August 9th, 2019



**Verona Area
School District**

"Every Student MUST Be Successful!"

The Final School Roof Joist!

This week has been very exciting and memorable week for the new Verona Area High School! The iconic orange beam that was signed by the 1,900 students and staff of the current Verona High school was set in the Music area of the new school. With the last pieces of roof decking being placed in this area next week, the entire roof structure is just about complete!

Aside from the roof structure being completed, finishes in the school continue with the staircases starting to be painted, and the epoxy flooring starting in the bathrooms. On site, the binder course is going down in many of the southern parking lots, sidewalks continue to be poured and topsoil is being placed around the fields for seed.

Looking ahead the kitchen equipment will start to be installed next week, starting with the coolers and hoods. On site, the softball concession stand roofing will be complete, along with starting to plant plants and continuing binder course.

The Past Week:

- Binder Course in the south parking lot
- Finished level 3 drywall
- Sidewalks in the southern parking lots
- Taping in the West Atrium

Upcoming :

- PAC Slope Seating Slab on Grade Pour
- Painting West side of the Atrium
- Kitchen Coolers install
- Carpet on level 3



The photo above was a group of students and staff at the Verona Area High School that signed the memorable orange beam on May 1st. The orange signed beam was placed as part of the future music roof structure last week.



DID YOU KNOW?

A square foot of drywall weighs approximately 2.3 pounds per square foot. In the New Verona Area High School there is 310,000 square feet of drywall being put in. This means that throughout the school there is 716,100 pounds of drywall, that is the same as a Boeing 777-300 airplane!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com


Findorff

EXECUTIVE SUMMARY REPORT


Verona Area High School



August 9th, 2019

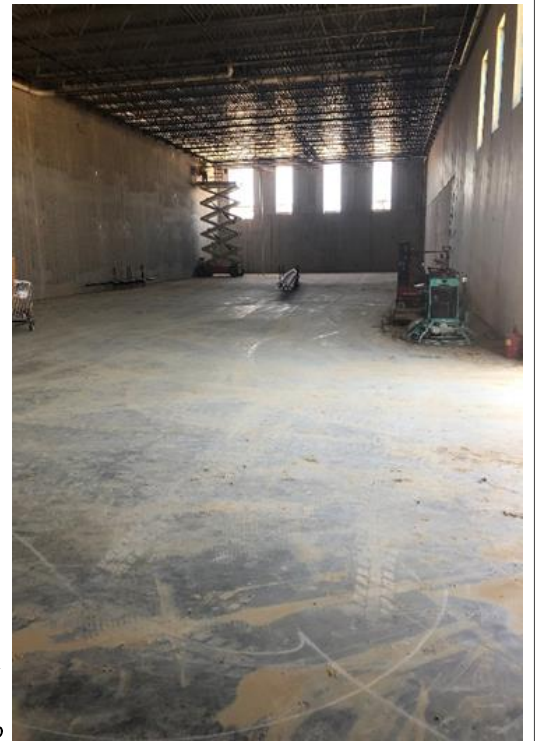

Above is a view of the Café section of the atrium that is currently being taped and prepared for paint. Top right is view of the gymnastic section of the fieldhouse slab on grade that was poured.

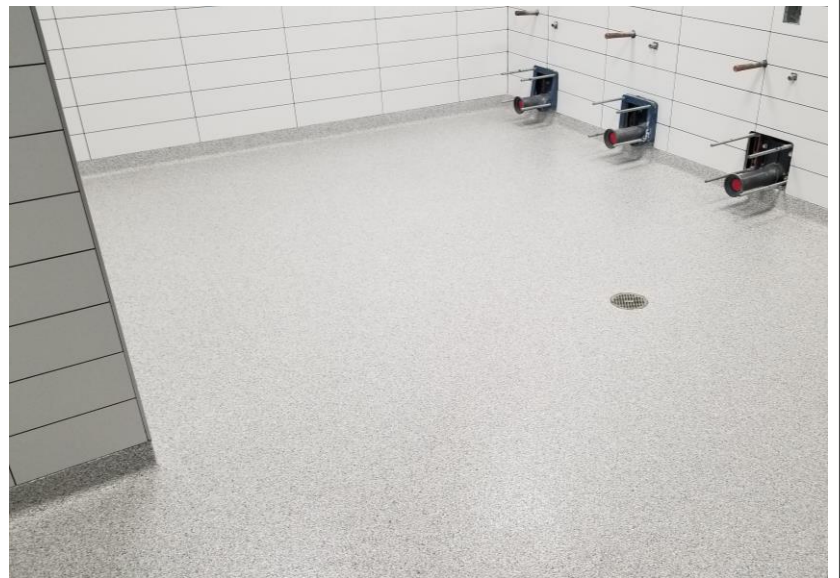

Above is a photo of one of the staircase corridors which is currently being painted with a vibrant yellow, orange and the top a teal color. To the right is a view of one of the epoxy bathroom floors on the third floor. The toilets and sinks will start to be installed within the next few weeks!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT

Verona Area High School



August 9th, 2019



Top: The Binder course for the South Parking lots are complete! Next week we will start with topsoil and planting plants in the islands of the parking lots. In the upper right photo, the topsoil is being placed around the softball fields with grass seed following. Above is a picture of the football ticket booth block that was complete this week. To the left is a picture of the pre-function area of the fieldhouse. The orange metal panels started to be installed this week bringing the enclosure closer to being complete!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff
