

EXECUTIVE SUMMARY REPORT

Verona Area High School



September 6th, 2019



**Verona Area
School District**

"Every Student MUST Be Successful!"

Scoreboards are Ready for Game Time!

The finishes have progressed tremendously in the past two weeks! The third floor has made significant progress as the door and hardware installation began, the perimeter ceiling tile started, and the lights are lighting up the classroom ceilings. In the kitchen area, the hoods finished install and the kitchen coolers concrete was completed. Finally, in the warm community pool, the first concrete floor was poured! On site progress continued while the football and softball varsity and JV scoreboards were installed, and the baseball dugouts and press box foundations were poured. In addition, the exterior social stair is almost complete, and plants are ongoing throughout the site.

In the following weeks, the atrium collaboration stair will start to be installed and casework installation will begin on the second floor! On site, the football field will start to look different as the football bleachers start next week and the artificial turf installation begins. In addition the baseball fields are starting irrigation install and masonry dugout and press box.

The Past Week:

- Music Area roof complete
- Warm Pool floor Concrete poured
- Soccer retaining wall complete
- Soccer Press box Masonry

Coming Up in the Week Ahead:

- Ceiling tiles on level 3
- Atrium Collaboration stair
- Fieldhouse Painting



The image above is the new Verona Area High School Football Scoreboard that was installed last week! Below is an image of the warm pool concrete floor that was poured this week. Next will be the walls for the pool and then backfill.



DID YOU KNOW?

The largest scoreboard is found in Texas in the Dallas Cowboys football stadium and it measures 161 feet by 71 feet. To compare the football scoreboard at the New Verona Area High School measures 24 feet by 15 feet.

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT

Verona Area High School




September 6th, 2019



Above: Wood Doors and hardware are started install on the third floor. Each door comes with a unique hardware set that must be installed individually. Below is a view of a hallway on the second floor that was painted a vibrant yellow.



Top: A view from above shows the music area roof complete. Now only the pool area is left to finish for roofing! Below the top photo is an image of the kitchen hood that have been installed along with a view of the kitchen coolers. To the right is one of the sinks that were installed after the countertops were completed on the third floor.

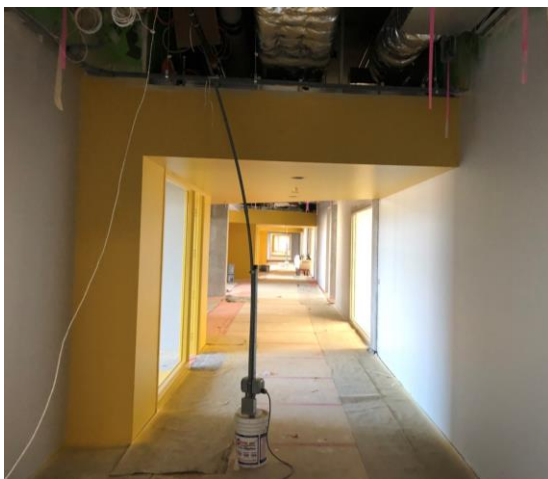

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT

PROJECT NAME



September 6th, 2019



Top: The view of the Verona Area High School Site is coming together as the grass grows, the football field is prepped for turf within the next weeks, and bleachers are ready for install. Above: The baseball field is starting topsoil and masonry, next will be irrigation and fencing. Upper Right is a view of the soccer retaining wall that completed this week. Right: A future student hangout is almost complete as the last steps of the exterior social stair are being poured next week!

QUESTIONS? Please contact Project Manager Aaron Zutz at 608.441.6891 or azutz@findorff.com

Findorff
